

Board Update September 5th, 2023



Park Rapids Additions and Renovations PARK RAPIDS PUBLIC SCHOOLS

Agenda



- <u>High School Updates</u>
- <u>Century Site Improvement Updates</u>
- Bus Garage Updates
- <u>Upcoming</u>
- Overall Schedule
- <u>Q&A</u>



- Construction Continues!
- Area 5 Footing & Foundation Work Continues
- Area 1 Structural Steel Erection Continues
- Area 1 Cold-Formed Framing Commenced
- Area 4 (New Gymnasium) Precast Installation to Commence
- Area 5 Utility Work Continued
- The Existing Fuel Tank was Removed
- The Temp. Road from Huntsinger to Helten was Completed
- Tracking On Schedule
















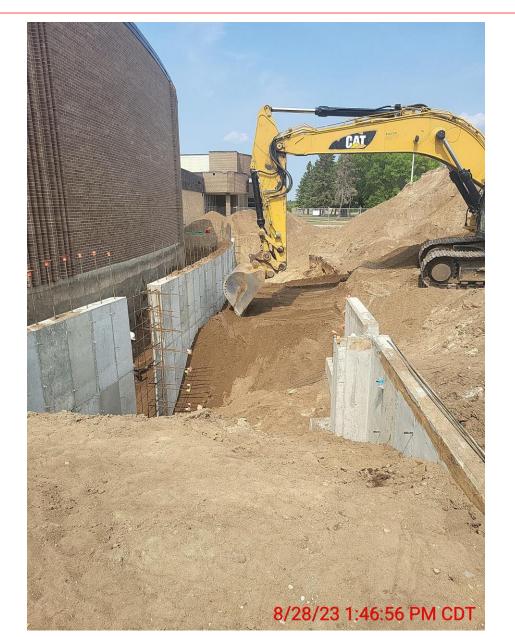








- Construction Is Substantially Completed!
- Punchlist Items Continuing to be Addressed
- The Existing Loop was Completed
- The NE Infiltration Basin was Completed
- Successful Project Overall







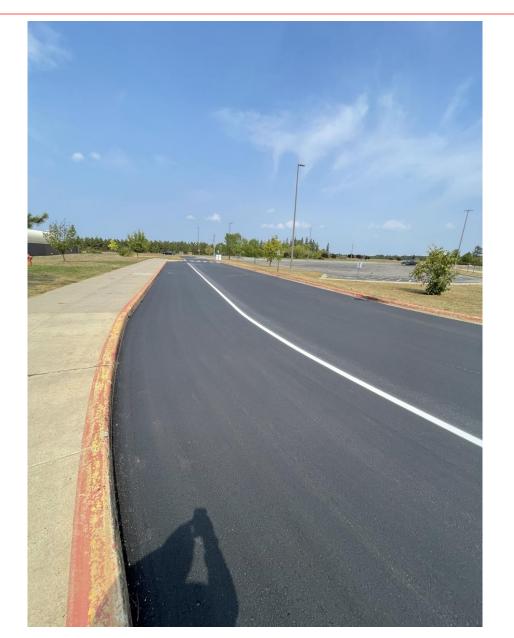












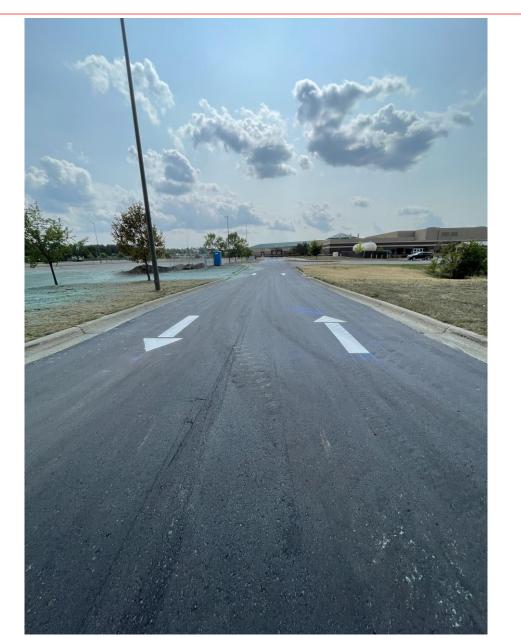



- Construction Continues
- Foundation Work Continues at the Bus Storage
- Maintenance PEMB Erection Continues
- Tracking on Schedule





















- Century Renovations Construction Documents
 - Will be bid in early '24
- Continue to Progress Through Construction



- Elementary Parent Pick-up / Drop-off Substantially Completed
- Bus Garage Summer of '23 w/ Substantial Completion Early February of '24, Sitework Spring of '24
- Elementary Renovations Summer of '24
- Secondary Additions Commence Summer of '23 Complete August of '24
- Secondary Additions (ALC/Trans./Kitchen) Commence Summer of '24 and Complete May of '25 (Reference Phasing Plan)
- Secondary Phase 1 Renovations Summer of '24 (Reference Phasing Plan)
- Secondary Phase 2 Renovations Summer of '25 (Reference Phasing Plan)

Questions?

