



# Board Update

## August 7<sup>th</sup>, 2023



Park Rapids Additions and Renovations  
PARK RAPIDS PUBLIC SCHOOLS

## Agenda

---



- High School Updates
- Century Site Improvement Updates
- Bus Garage Updates
- Upcoming
- Overall Schedule
- Review Proposal Request #1 for Approval – PR High School Improvements Project
- Q&A

Park Rapids Additions and Renovations

## High School Improvements

---



- Construction Continues!
- Area 5 (HS Admin. Addition) is Clear & Grubbed
- Area 1, 2 Foundations Complete
  - Area 4 (New Gymnasium) Nearing Completion
- Re-roofing Nearly Complete
- Utility Work
- Tracking On Schedule

# High School Improvements



# High School Improvements



# High School Improvements

---



# High School Improvements



8/1/23 8:38:30 AM CDT

# High School Improvements

---





## Century Site Improvements

---



- Construction Nears Completion!
- All Concrete Work Complete is Complete
- Final Grading & Proof Roll Complete
- Asphalt Paving Nearing Completion
- Tracking on Schedule

# Century Site Improvements



# Century Site Improvements

---



# Century Site Improvements

---



# Century Site Improvements

---



# Century Site Improvements

---



## Bus Garage

---



- Construction Continues
- Underground Plumbing is Complete
- Foundation Work Continues
- Maintenance PEMB arrived 7/28
- Tracking on Schedule

# Bus Garage





# Bus Garage

---



# Bus Garage

---



# Bus Garage



## Upcoming

---



- Century Renovations – Construction Documents
  - Will be bid in early '24
- Continue to Progress Through Construction on All Projects

## Overall Schedule

---



- Bus Garage – Summer of '23 w/ Substantial Completion Early February of '24, Sitework Spring of '24
- Elementary Parent Pick-up / Drop-off – Summer of '23
- Elementary Renovations – Summer of '24
- Secondary Additions – Commence Summer of '23 – Complete August of '24
- Secondary Additions (ALC/Trans./Kitchen) – Commence Summer of '24 and – Complete May of '25 (Reference Phasing Plan)
- Secondary Phase 1 Renovations – Summer of '24 (Reference Phasing Plan)
- Secondary Phase 2 Renovations – Summer of '25 (Reference Phasing Plan)



ICS  
 1331 Tyler Street NE, Suite 101  
 Minneapolis, Minnesota 55413  
 P: (763) 354-2670  
 F: (763) 780-2866

Project: S21144C - ISD #309 - Park Rapids High School Facility Improvements

401 Huntsinger Drive  
 Park Rapids, Minnesota 56470  
 P: 218-237-6500

**PR #1 - MNDOLI Required Plan Changes**

**Origin:**

**Date Created:** 3/16/2023      **Created By:** Justin Maaninga  
**Status:** Open      **Scope:** TBD  
**Type:** TBD      **Change Reason:** Design Development  
**Description:** PR #1 - State Plan Review Changes

**If it is a no cost change to you, please indicate as such.**

**Attachments:** [PR #1 - Plan Review Changes.pdf](#)

**CHANGE EVENT LINE ITEMS**

Budget Code	Vendor / Contract	Prime CCO	ROM	RFQ	Commit.	Budget Mod.
05-5.01.O	Reierson Construction		\$0.00	\$0.00		
WS 01 Earthwork - Reierson.Other	SC-S21144C-001					
Description: PR #1 - Plan Review						
05-5.01.5.O	Howard's Driveway Paving, Inc.		\$0.00	\$0.00		
WS 01.5 Asphalt - Howards.Other	SC-S21144C-01.5					
Description: PR #1 - Plan Review						
05-5.02.O	TNT Construction Group, LLC		\$0.00	\$3,697.49		
WS 02 Concrete - TNT.Other	SC-S21144C-002					


Budget Code	Vendor / Contract	Prime CCO	ROM	RFQ	Commit.	Budget Mod.
Description: PR #1 - Plan Review						
05-5.03.O	Johnson-Nelson Masonry		\$0.00	\$51,797.00		
WS 03 Masonry - JN	SC-S21144C-003					
Masonry.Other						
Description: PR #1 - Plan Review						
05-5.04.O	Wells Concrete		\$0.00	\$0.00		
WS 04 Precast Concrete -	SC-S21144C-004					
Wells.Other						
Description: PR #1 - Plan Review						
05-5.05.O	Integrity Steel Supply, LLC		\$0.00	\$0.00		
WS 05 Steel Material -	SC-S21144C-005					
Integrity.Other						
Description: PR #1 - Plan Review						
05-5.06.O	Innovative Builders of Alexandria, Inc.		\$0.00	\$0.00		
WS 06 Steel Installation -	SC-S21144C-006					
Innovative ERectors.Other						
Description: PR #1 - Plan Review						
05-5.07.O	Thelen Heating & Roofing, Inc.		\$0.00	\$800.00		
WS 07 Roofing - Thelen.Other	SC-S21144C-007					
Description: PR #1 - Plan Review						
05-5.7.5.O	Haataja Contracting		\$0.00	\$0.00		
	SC-S21144C-07.5					

Budget Code	Vendor / Contract	Prime CCO	ROM	RFQ	Commit.	Budget Mod.
WS 7.5 Metal Wall Panels - Haataja.Other Description: PR #1 - Plan Review						
05-5.08.O	Woodside Industries, Inc.		\$0.00	\$(1,814.64)		
WS 08 Casework - Woodside.Other SC-S21144C-008 Description: PR #1 - Plan Review						
05-5.09.O	Haataja Contracting		\$0.00	\$7,849.82		
WS 09 General Construction - Haataja.Other SC-S21144C-009 Description: PR #1 - Plan Review						
05-5.10.O	Sell Hardware		\$0.00	\$(4,826.00)	\$(4,826.00)	
WS 10 Doors, Frames, Hdwr - Sell.Other SC-S21144C-010 Description: PR #1 - Plan Review						
05-5.11.O	Fergus Drywall, Inc.		\$0.00	\$4,501.00		
WS 11 Steel Stud & Drywall - Fergus.Other SC-S21144C-011 Description: PR #1 - Plan Review						
05-5.12.O	Fransen Decorating, Inc.		\$0.00	\$4,430.00		
WS 12 Paint & Wall Coverings - Fransen.Other SC-S21144C-012 Description: PR #1 - Plan Review						



Budget Code	Vendor / Contract	Prime CCO	ROM	RFQ	Commit.	Budget Mod.
05-5.13.O	United Glass, Inc.		\$0.00	\$0.00		
WS 13 Doors, Windows, Glazing -	SC-S21144C-013					
United Glass.Other						
Description:						
PR #1 - Plan Review						
05-5.14.O	Arnquist Carpets Plus		\$0.00	\$20,522.50		
WS 14 Tile & Flooring -	SC-S21144C-014					
Arnquist.Other						
Description:						
PR #1 - Plan Review						
05-5.15.O	FLR Sanders, Inc.		\$0.00	\$0.00		
WS 15 Athletic Wood Flooring - FLR	SC-S21144C-015					
Sanders.Other						
Description:						
PR #1 - Plan Review						
05-5.16.O	Dow Acoustics, Inc.		\$0.00	\$1,015.00		
WS 16 Acoustic Ceilings -	SC-S21144C-016					
Dow.Other						
Description:						
PR #1 - Plan Review						
05-5.17.O	Culinex		\$0.00	\$1,344.34		
WS 17 FS Fixed Equip -	SC-S21144C-017					
Culinex.Other						
Description:						
PR #1 - Plan Review						
05-5.18.O	Culinex		\$0.00	\$0.00		
WS 18 FS Loose Equip -	SC-S21144C-018					
Culinex.Other						

Budget Code	Vendor / Contract	Prime CCO	ROM	RFQ	Commit.	Budget Mod.
Description: PR #1 - Plan Review						
05-5.20.O	Masters Plumbing Heating and Cooling		\$0.00	\$93,369.69		
WS 20 Mechanical - Masters.Other	LLC SC-S21144C-020					
Description: PR #1 - Plan Review						
05-5.21.O	Ace Electric & Lighting		\$0.00	\$0.00		
WS 21 Electrical - Ace.Other	SC-S21144C-021					
Description: PR #1 - Plan Review						
05-5.22.O	Cosney Corporation		\$0.00	\$0.00		
Ws 22 Wood Lab Equip - Cosney.Other	SC-S21144C-022					
Description: PR #1 - Plan Review						
05-5.19.O	Absolute Fire Protection		\$0.00	\$1,960.00		
WS 19 Fire Suppression - AFP.Other	SC-S21144C-019					
Description: PR #1 - Plan Review						
<b>Grand Totals</b>		<b>\$0.00</b>	<b>\$0.00</b>	<b>\$184,646.20</b>	<b>\$(4,826.00)</b>	<b>\$0.00</b>



**SHEET MATERIAL ID LIST**


MATERIAL ID	SPEC SECTION & DESCRIPTION
BBALL-1	11 6623 - BASKETBALL BACKSTOP
BBALL-2	
BENCH-10	10 5113 - LOCKER ROOM BENCH - ACCESSIBLE
CMU-2	04 2008 - SCORED-FACE STANDING GREY CMU
CLUBCL-2	10 2113 - CLUBCLUB CURTAIN AND TRACK
FBRKT-1	10 4400 - FIRE EXTINGUISHER BRACKET
FIRE DR-3	08 3513 - FIRE DOOR - EXIT HARDWARE BOTH SIDES
FL HATCH-1	08 3300 - FLOOR HATCH
GYMCRTN-1	11 6623 - DIVIDER CURTAIN
WALL PAD-1	11 6623 - WALL PADDING

**FLOOR PLAN KEYNOTES**


KEYNOTE	DESCRIPTION
01	MODIFY FLOORING AND CEILING AS REQUIRED TO FACILITATE WALL CONSTRUCTION
02	LAVATORY AND MIRROR, SEE SHEET G120.
03	PATCH AND REPAIR GYPSUM/PLASTER WALLS WHERE DAMAGED FROM WALL REMOVAL
04	MODIFY EXISTING FLOORING AS REQUIRED TO INSTALL NEW WALL/CASEWORK
05	PATCH AND REPAIR AND INFILL EXISTING CMU WALL WHERE DAMAGED
06	PATCH INFILL AND REPAIR WALL WHERE FIRE EXTINGUISHER CABINET REMOVED
07	EXISTING CLOCK AND SPEAKER BASE TO BE REMOVED BY ELECTRICAL. PROVIDE SMF-2 TO COVER EXISTING OPENING. PAINT TO MATCH WALL COLOR.
08	AUTOMATIC DOOR OPERATOR ACTUATOR, 34" A.F.F.
09	AUTOMATIC DOOR OPERATOR ACTUATOR - MULLION MOUNT, 34" A.F.F.
10	CARD ACCESS CONTROL READER. SEE ELECTRICAL.
11	DOOR RELEASE CALL STATION. SEE ELECTRICAL.
13	PATCH AND REPAIR WALL WHERE DRINKING FOUNTAIN REMOVED
14	PATCH AND REPAIR WALL WHERE CABINET UNIT HEATER REMOVED
15	GYM FLOOR STRIPING TO INCLUDE TWO BASKETBALL COURTS AND THREE VOLLEYBALL COURTS; COORDINATE WITH ARCHITECT
16	PATCH AND REPAIR CMU WALL WHERE WALL DAMAGED FROM REMOVAL. PAINT TO MATCH EXISTING
17	INSTALL SALVAGED AED
18	INSTALL SALVAGED BUILDING PLAQUE
19	PROVIDE NEW DOOR NUMBER SIGNAGE. SEE SHEET G133 AND A620
20	SALVAGED LOCKERS RELOCATED BY CONTRACTOR
21	SLOPE FLOOR 1/4" TO NEW TRENCH DRAIN, SEE STRUCTURAL AND MECHANICAL FOR ADDITIONAL INFORMATION
22	SLOPE FLOOR 1/4" TO NEW DRAIN
23	INSTALL SALVAGED BRICK AS REQUIRED
24	COORDINATE ALL FLOOR DRAINS AND SLOPES WITH MECHANICAL, STRUCTURAL, AND FOOD SERVICE.
25	PROVIDE HOLLOW METAL LIGHT FIX FOR MARRON VISION LIGHT TO MATCH DOOR PANEL TYPE 'N' FOR EACH LEAF. GLAZING TO BE GL-1
26	AT ALL DETERIORATED CMU EXTERIOR FACE SHELL LOCATIONS, REMOVE DEBRIS AS REQUIRED AND GROUT ALL CORES SOLID WITH CONCRETE
27	INFILL EXISTING OPENING WITH SALVAGED BRICK
28	PATCH AND GRIND EXISTING HARDWARE HOLES PRIOR TO PAINTING FRAME
29	PROVIDE BLOCKING FOR OWNER SUPPLIED SIGN CUTTER
30	PATCH AND REPAIR WALL WITH SALVAGED BRICK WHERE FIRE DEPARTMENT HOOKUP WAS REMOVED

**FLOOR PLAN GENERAL NOTES**

- A. SEE SHEET G120 FOR TYPICAL MOUNTING HEIGHTS INCLUDING ACCESSORIES AND ACCESSIBILITY.
- B. ALL PARTITION TYPES ARE "A4" TYPICALLY UNLESS OTHERWISE NOTED.
- C. PROVIDE SOAP DISPENSERS AND PAPER TOWEL DISPENSER AT ALL SINKS U.N.O.
- D. PROVIDE BLOCKING AT WALL-MOUNTED SHELVES AND STORAGE UNITS, MARKER BOARDS, BULLETIN BOARDS, TACK BOARDS, MONITORS AND OTHER CONTRACTOR OR OWNER FINISHED WALL-MOUNTED ITEMS. SEE INTERIOR ELEVATIONS FOR SCOPE OF BLOCKING LOCATIONS AT MARKER BOARDS.
- E. FOR ALL FLOORING CHANGES BETWEEN ROOMS, TRANSITION SHALL OCCUR AT CENTERLINE OF DOOR PANEL. SEE SHEET A600 FOR TYPICAL FLOORING TRANSITIONS.
- F. PROVIDE BULLNOSE ON ALL CMU OUTSIDE CORNERS U.N.O.
- G. FOR INTERIOR METAL STUD CONSTRUCTION ALL DIMENSIONS ARE TO FACE OF METAL STUDS UNLESS NOTED OTHERWISE.
- H. ALL DIMENSIONS INDICATED AS 'CLEAR' ARE TO FACE OF FINISH (GYPSUM, TILE, ETC.).
- I. ALL MASONRY DIMENSIONS ARE TO FACE OF MASONRY UNLESS NOTED OTHERWISE.
- J. ALL EXTERIOR OPENING DIMENSIONS ARE ROUGH OPENINGS.
- K. COORDINATE ALL FLOOR OPENING DIMENSIONS AND CLEARANCES FOR DUCTWORK W/ MECHANICAL CONTRACTOR - TYPICAL.
- L. COORDINATE AND/OR CONFIRM ANY DIMENSIONAL DISCREPANCIES WITH ARCHITECT PRIOR TO INSTALLATION.
- M. ALL NEW FLOOR ASSEMBLIES TO BE F.L1 UNLESS NOTED OTHERWISE.
- N. SEE THE DEMOLITION LEGEND ON THE DEMOLITION PLANS FOR LOCATIONS WHERE FLOOR LAB INFILL REQUIRED.
- O. FRAMING DETAILS FOR CANNOPES 10'-0" ABOVE FIRST FLOOR LEVEL CALLED OUT ON THE RCP DRAWINGS A701-A709.
- P. LIMITED SCOPE AREA

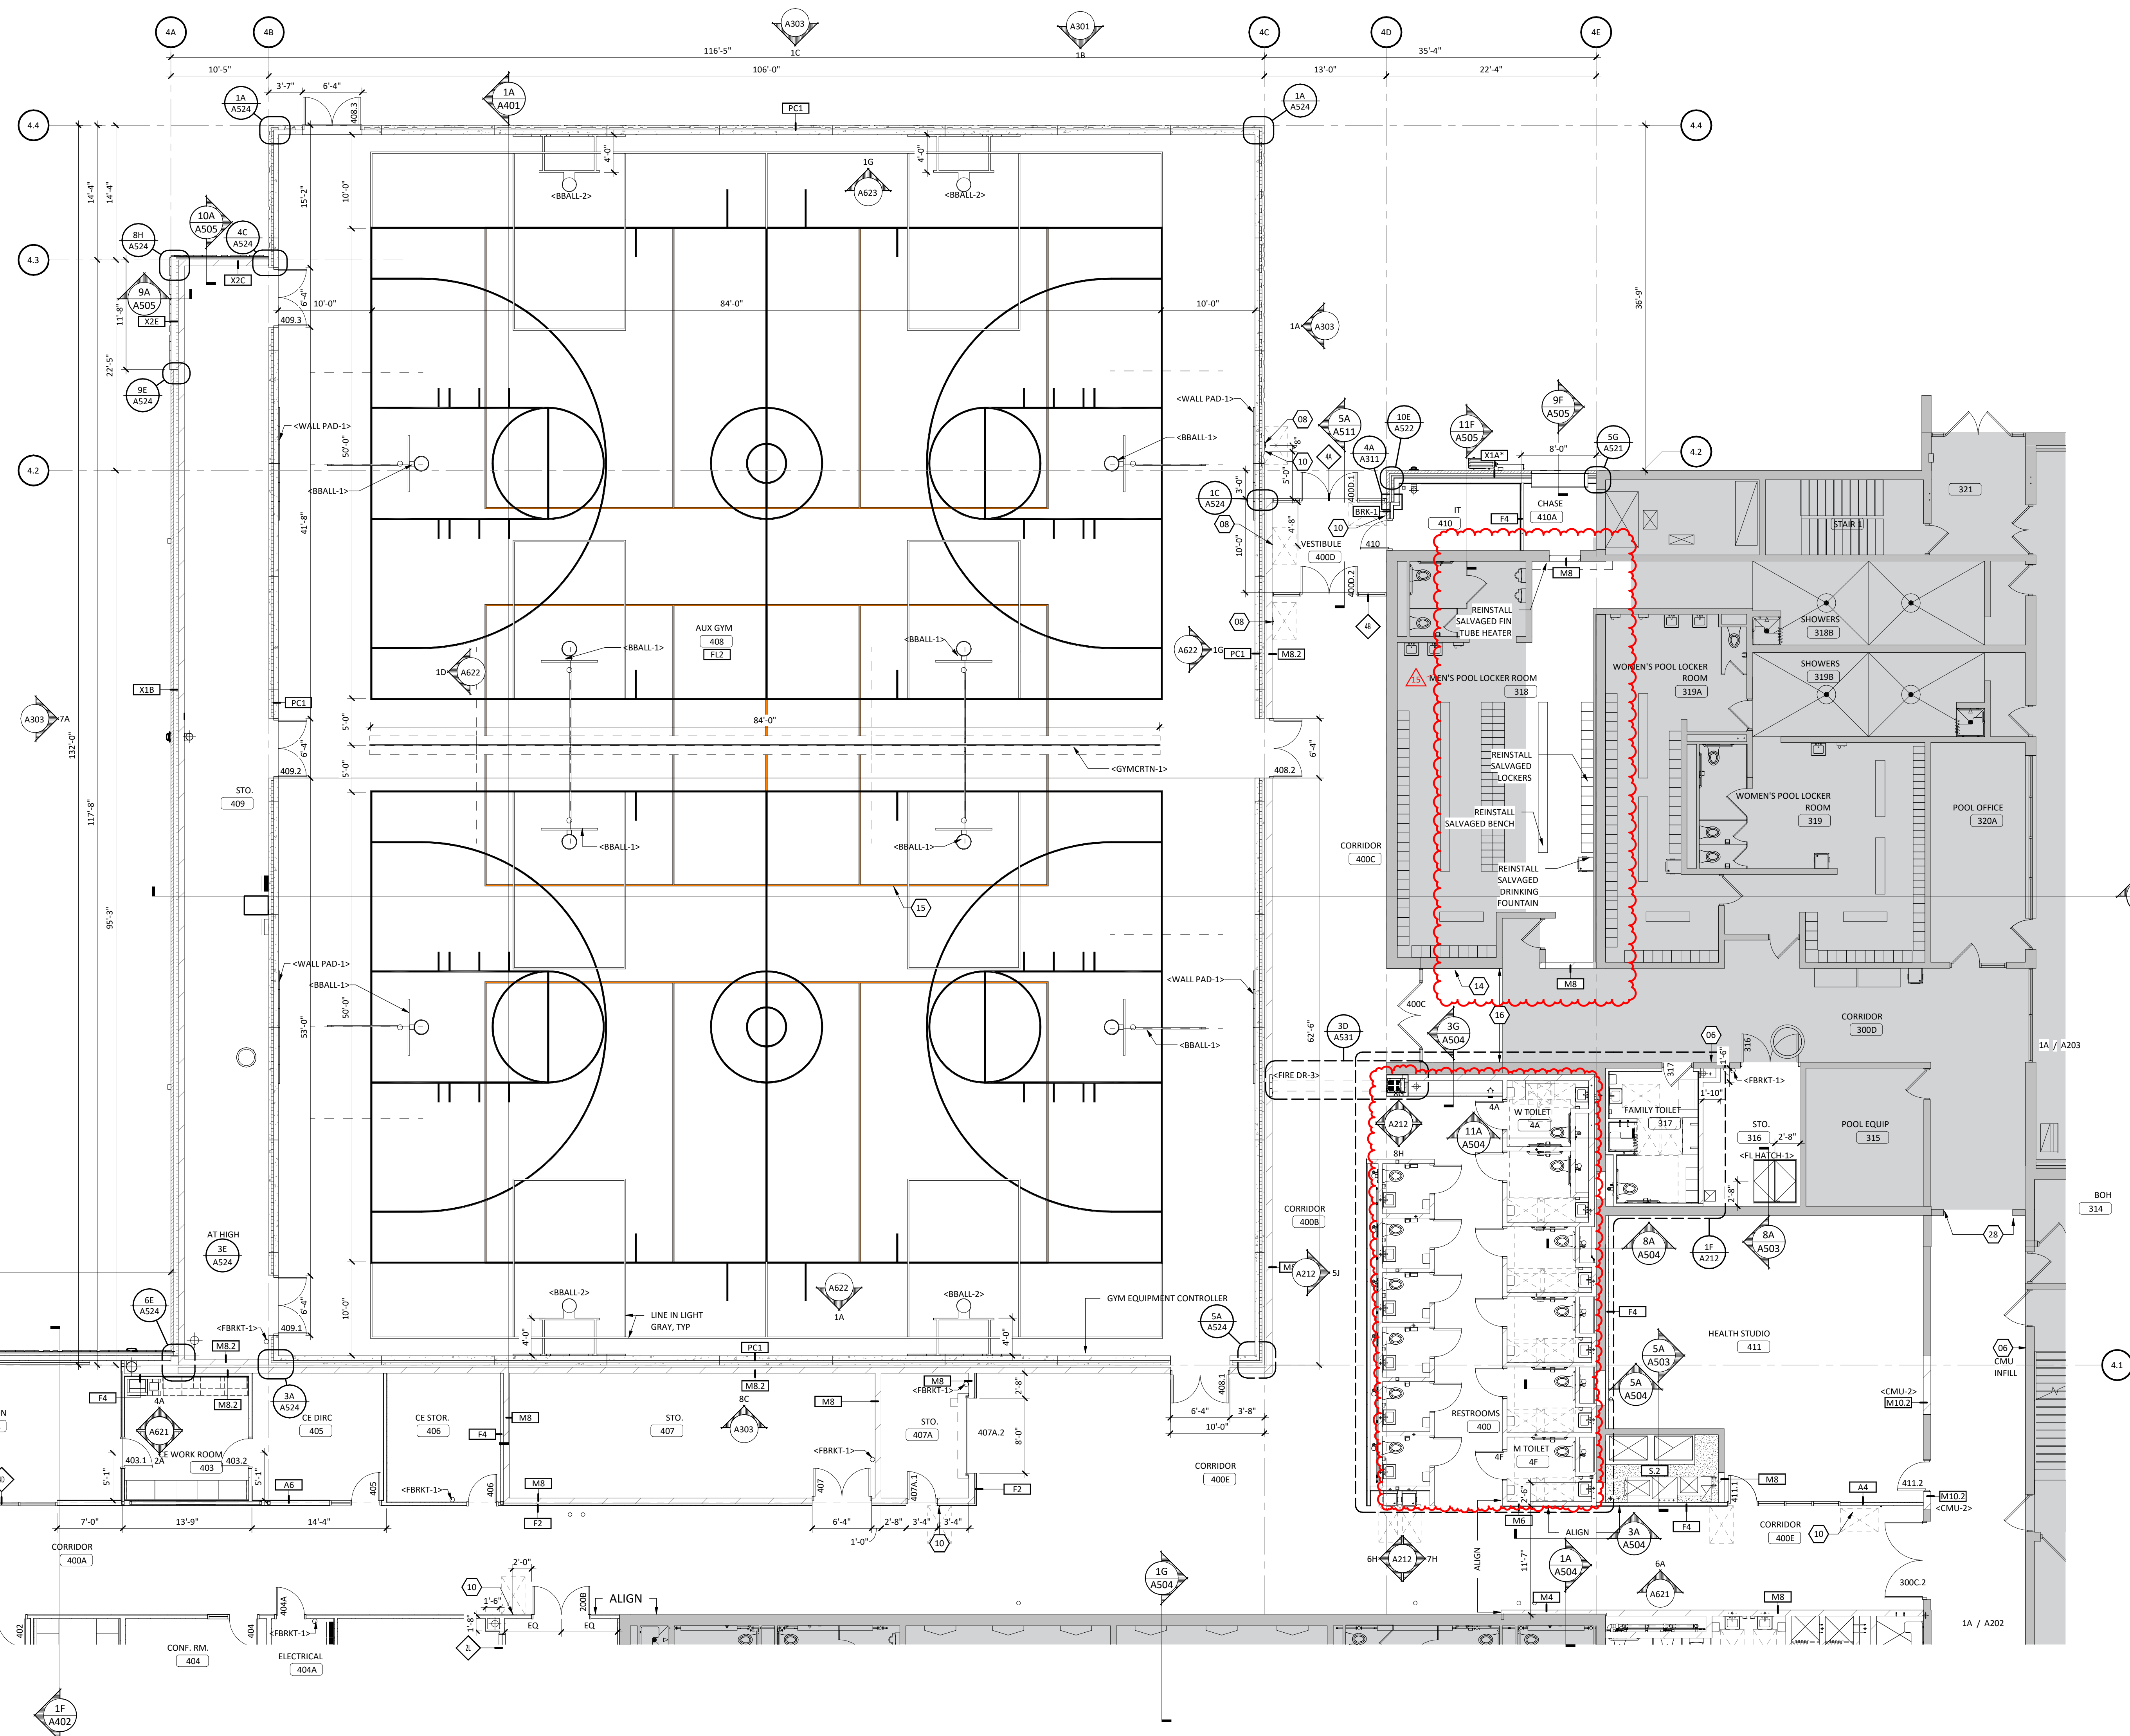

**1A A204 FIRST FLOOR - AREA 4**  
SCALE: 1/8" = 1'-0"

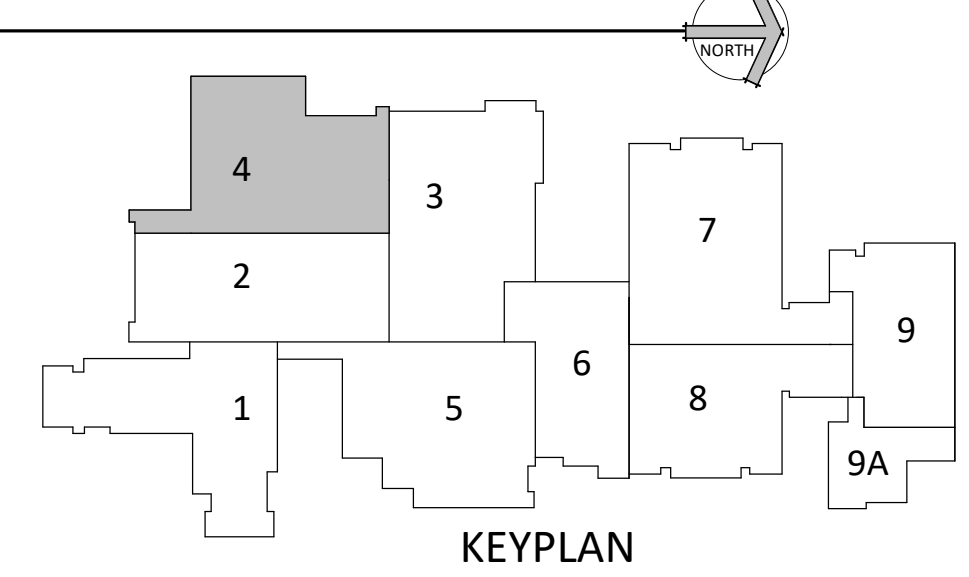

Project Name:



**PARK RAPIDS HIGH SCHOOL**

Project Location:  
**PARK RAPIDS, MN**

© 2022 ICS Consulting

THESE DOCUMENTS HAVE BEEN PREPARED SPECIFICALLY FOR THE PROJECT ONLY. THEY ARE NOT TO BE REPRODUCED OR USED FOR OTHER PROJECTS OR OTHER LOCATIONS WITHOUT THE EXPRESS WRITTEN APPROVAL AND PARTICIPATION OF ICS Consulting.

MARK	DATE	REVISION
1	01/05/23	ADDENDUM #1
2	01/17/23	ADDENDUM #3
3	06/02/23	PR 001
4	04/19/23	PR 004
5	04/19/23	PR 006
15	06/05/23	PR 010
16	06/05/23	PR 011


I hereby certify that this plan, specification, or report was prepared by me or under my direct supervision, and that I am a duly Licensed Architect under the laws of the State of Minnesota.

Signature:  
Printed Name: David A. Leapoldt  
Date: 12/02/2022 Reg. No.: 20052

Project Information:  
Project No.: 19168  
Drawn By: MPN  
Checked By: WAL  
Date: 12/02/22

Sheet Title:  
FIRST FLOOR - AREA 4

Sheet Number:  
**A204**

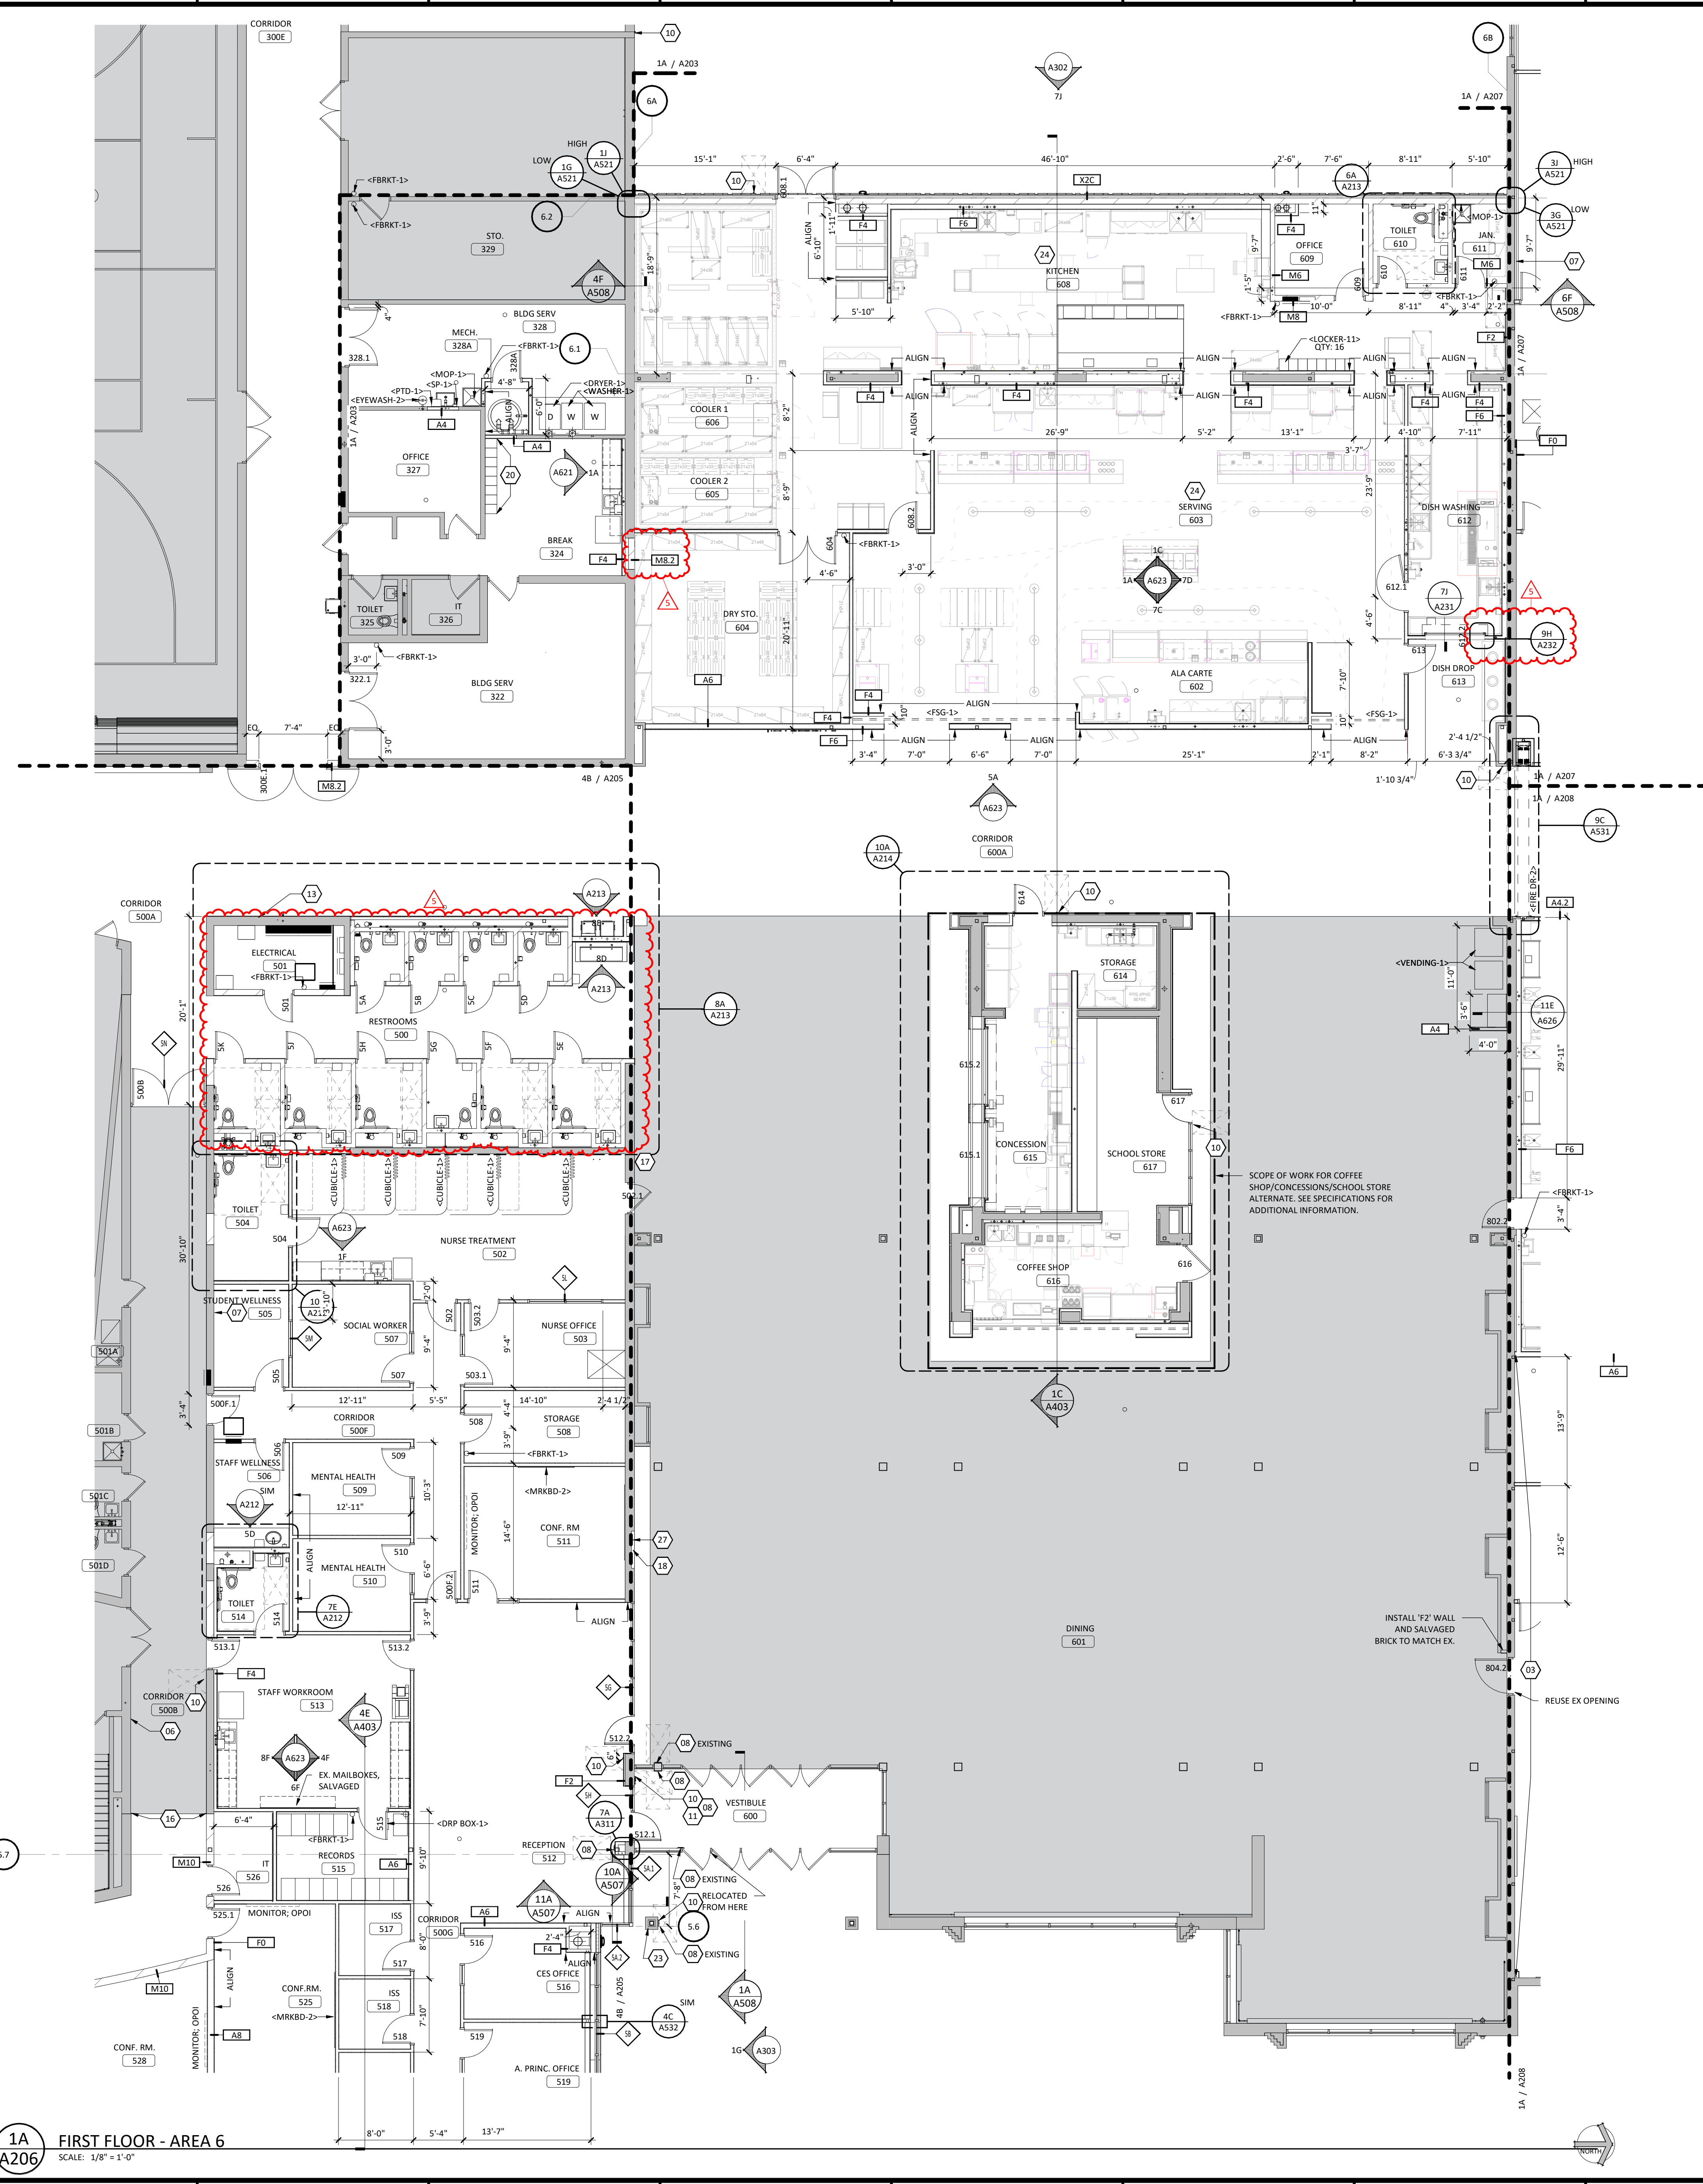

### SHEET MATERIAL ID LIST

MATERIAL ID	SPEC SECTION & DESCRIPTION
CUBICLE-1	10 2113 - CUBICLE CURTAIN AND TRACK
DRP BOX-1	10 5500 - THROUGH DOOR DROP BOX
DRYER-1	DRYER, OPOI
EYEWASH-2	22 4516 - WALL MOUNTED EYEWASH, SEE PLUMBING DRAWINGS
FBFRKT-1	10 4400 - FIRE EXTINGUISHER BRACKET
FIRE DR-2	08 3513 - FIRE DOOR, EXIT HARDWARE ONE SIDE
FSG-1	10 8211 - ROLLING COILED WIRE SECURITY GRILLE
LOCKER-11	10 5113 - METAL LOCKERS - TWO TIER 12" W X 15" D X 36" H
MOP-1	10 2800 - UTILITY SHELF AND MOP HOLDER
MRRBD-2	10 1101 - MARKER BOARD
PTD-1	PAPER TOWEL DISPENSER, OPOI
SP-1	SOAP DISPENSER, WALL MOUNT, OPOI
VENDING-1	VENDING MACHINE, OPOI
WASHER-1	WASHING MACHINE, OPOI

### FLOOR PLAN KEYNOTES

KEYNOTE	DESCRIPTION
01	MODIFY FLOORING AND CEILING AS REQUIRED TO FACILITATE WALL CONSTRUCTION
02	LAVATORY AND MIRROR, SEE SHEET G120.
03	PATCH AND REPAIR GYPSUM/PLASTER WALLS WHERE DAMAGED FROM WALL REMOVAL
04	MODIFY EXISTING FLOORING AS REQUIRED TO INSTALL NEW WALL/CASEWORK
05	PATCH AND REPAIR AND INFILL EXISTING CMU WALL WHERE DAMAGED
06	PATCH INFILL AND REPAIR WALL WHERE FIRE EXTINGUISHER CABINET REMOVED
07	EXISTING CLOCK AND SPEAKER BASE TO BE REMOVED BY ELECTRICAL. PROVIDE SMF-2 TO COVER EXISTING OPENING. PAINT TO MATCH WALL COLOR.
08	AUTOMATIC DOOR OPERATOR ACTUATOR, 24" A.F.F.
09	AUTOMATIC DOOR OPERATOR ACTUATOR - MULLION MOUNT, 34" A.F.F.
10	CARD ACCESS CONTROL, READER, SEE ELECTRICAL.
11	DOOR RELEASE CALL STATION, SEE ELECTRICAL.
12	PATCH AND REPAIR WALL WHERE DRINKING FOUNTAIN REMOVED
13	PATCH AND REPAIR WALL WHERE CABINET UNIT HEATER REMOVED
14	PATCH AND REPAIR CMU WALL WHERE WALL DAMAGED FROM REMOVAL. PAINT TO MATCH EXISTING
15	GYM FLOOR STRIPING TO INCLUDE TWO BASKETBALL COURTS AND THREE VOLLEYBALL COURTS, COORDINATE WITH ARCHITECT
16	PATCH AND REPAIR CMU WALL WHERE WALL DAMAGED FROM REMOVAL. PAINT TO MATCH EXISTING
17	INSTALL SALVAGED AED
18	INSTALL SALVAGED BUILDING PLAQUE
19	PROVIDE NEW DOOR NUMBER SIGNAGE, SEE SHEET G113 AND A620
20	SALVAGED LOCKERS RELOCATED BY CONTRACTOR
21	SLOPE FLOOR 1/4" TO NEW TRENCH DRAIN, SEE STRUCTURAL AND MECHANICAL FOR ADDITIONAL INFORMATION
22	SLOPE FLOOR 1/4" TO NEW DRAIN
23	INSTALL SALVAGED BRICK AS REQUIRED
24	COORDINATE ALL FLOOR DRAINS AND SLOPES WITH MECHANICAL, STRUCTURAL, AND FOOD SERVICE
25	PROVIDE HOLLOW METAL LIGHT KIT FOR NARROW VISION LIGHT TO MATCH DOOR PANEL TYPE "N" FOR EACH LEAF. GLAZING TO BE GL-1
26	AT ALL DETERIORATED CMU EXTERIOR FACE SHELL LOCATIONS, REMOVE DEBRIS AS REQUIRED AND GROUT ALL CORNER JOINTS WITH CONCRETE
27	INFILL EXISTING OPENING WITH SALVAGED BRICK
28	PATCH AND GRIND EXISTING HARDWARE HOLES PRIOR TO PAINTING FRAME
29	PROVIDE BLOCKING FOR OWNER SUPPLIED SIGN CUTTER
30	PATCH AND REPAIR WALL WITH SALVAGED BRICK WHERE FIRE DEPARTMENT HOOKUP WAS REMOVED

### FLOOR PLAN GENERAL NOTES

- SEE SHEET G120 FOR TYPICAL MOUNTING HEIGHTS INCLUDING ACCESSORIES AND ACCESSIBILITY.
- ALL PARTITION TYPES ARE "AF" TYPICALLY UNLESS OTHERWISE NOTED.
- PROVIDE SOAP DISPENSERS AND PAPER TOWEL DISPENSER AT ALL SINKS U.N.O.
- PROVIDE BLOCKING AT WALL-MOUNTED SHELVES AND STORAGE UNITS, MARKER BOARDS, BULLETIN BOARDS, TRACK BOARDS, MONITORS AND OTHER CONTRACTOR OR OWNER FURNISHED WALL-MOUNTED ITEMS. SEE INTERIOR ELEVATIONS FOR SCOPE OF BLOCKING LOCATIONS AT MARKER BOARDS.
- FOR ALL FLOORING CHANGES BETWEEN ROOMS, TRANSITION SHALL OCCUR AT CENTERLINE OF DOOR PANEL. SEE SHEET A600 FOR TYPICAL FLOORING TRANSITIONS.
- PROVIDE BULLNOSE ON ALL CMU OUTSIDE CORNERS U.N.O.
- FOR INTERIOR METAL STUD CONSTRUCTION ALL DIMENSIONS ARE TO FACE OF METAL STUDS UNLESS NOTED OTHERWISE.
- ALL DIMENSIONS INDICATED AS "CLEAR" ARE TO FACE OF FINISH (GYPSUM, TILE, ETC.).
- ALL MASONRY DIMENSIONS ARE TO FACE OF MASONRY UNLESS NOTED OTHERWISE.
- ALL EXTERIOR OPENING DIMENSIONS ARE ROUGH OPENINGS.
- COORDINATE ALL FLOOR OPENING DIMENSIONS AND CLEARANCES FOR DUCTWORK W/ MECHANICAL CONTRACTOR - TYPICAL.
- COORDINATE AND/OR CONFIRM ANY DIMENSIONAL DISCREPANCIES WITH ARCHITECT PRIOR TO INSTALLATION.
- ALL NEW FLOOR ASSEMBLIES TO BE FL1 UNLESS NOTED OTHERWISE.
- SEE THE DEMOLITION LEGEND ON THE DEMOLITION PLANS FOR LOCATIONS WHERE FLOOR SLAB INFILL REQUIRED
- FRAMING DETAILS FOR CANNOPHES 10' 0" ABOVE FIRST FLOOR LEVEL CALLED OUT ON THE RCP DRAWINGS A701, A709
- LIMITED SCOPE AREA

### REVISIONS

MARK	DATE	REVISION
1	01/05/23	ADDENDUM #1
2	01/17/23	ADDENDUM #3
5	06/02/23	PK 001


I hereby certify that this plan, specification, or report was prepared by me or under my direct supervision, and that I am a duly Licensed Architect under the laws of the State of Minnesota.


Signature: \_\_\_\_\_  
 Printed Name: David A. Leopoldt  
 Date: 12/02/2022 Reg. No.: 20052

**Project Information:**  
 Project No.: 19168  
 Drawn By: MPN  
 Checked By: WAL  
 Date: 12/02/22

**Sheet Title:**  
 FIRST FLOOR - AREA 6

**Sheet Number:**  
 A206

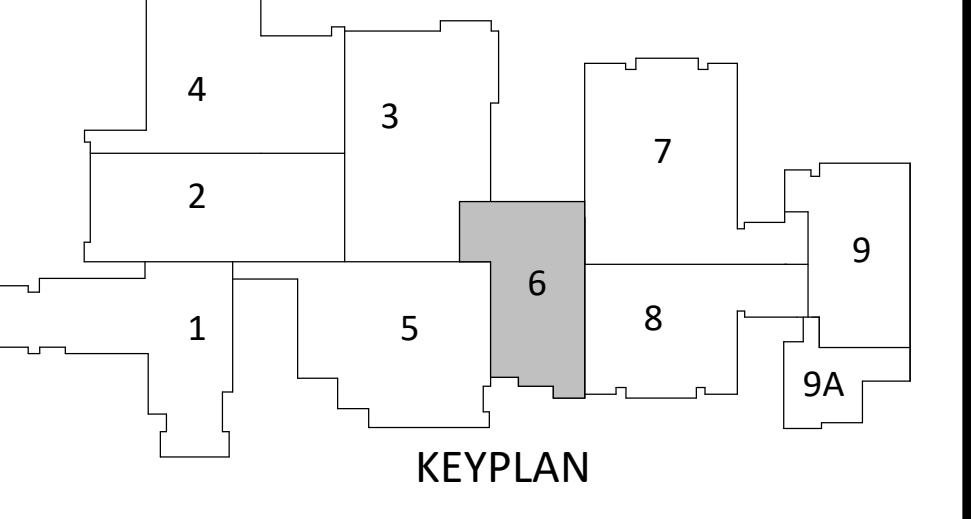

**Project Name:**  
  
 PARK RAPIDS  
 HIGH SCHOOL

**Project Location:**  
 PARK RAPIDS, MN

© 2022 ICS Consulting  
 THESE DOCUMENTS HAVE BEEN PREPARED SPECIFICALLY FOR THE PROJECT ONLY. THEY ARE NOT SUITABLE FOR USE ON OTHER PROJECTS OR OTHER LOCATIONS WITHOUT THE EXPRESS WRITTEN APPROVAL AND PARTICIPATION OF ICS Consulting.

I hereby certify that this plan, specification, or report was prepared by me or under my direct supervision, and that I am a duly Licensed Architect under the laws of the State of Minnesota.

Signature: \_\_\_\_\_  
 Printed Name: David A. Leopoldt  
 Date: 12/02/2022 Reg. No.: 20052

**Project Information:**  
 Project No.: 19168  
 Drawn By: MPN  
 Checked By: WAL  
 Date: 12/02/22

**Sheet Title:**  
 FIRST FLOOR - AREA 6

**Sheet Number:**  
 A206

## Proposal Request #1 MNDOLI Required Plan Changes - Recommendation



- Recommend approving the overall pricing from the multiple contractors in the grand total amount of \$184,646.20, for Proposal Request #1, MNDOLI Required Plan Review Changes.

Park Rapids Additions and Renovations

Questions?

The logo for ICS (International Chemical Safety Council) features a stylized vertical bar on the left, followed by the letters 'ICS' in a bold, dark blue, sans-serif font. The 'I' is a simple vertical bar, the 'C' is a thick, rounded shape with a white outline, and the 'S' is a thick, rounded shape with a white outline.
